

Date: Thursday, 1/18/2007 3:21:00 PM
 User: Kim Johnston

Process Sheet

Customer : CU-DAR001 Dart Helicopters Services	Drawing Name : 206B AFT X-TUBE
Job Number : 30318	
Estimate Number : 12347	
P.O. Number : N/A	Part Number : D206667201
This Issue : 1/18/2007 S.O. No. : N/A	Drawing Number : D206-667-241 REV B
Prsht Rev. : NC	Project Number : N/A
First Issue : N/A Type : LANDING GEAR	Drawing Revision : B
Previous Run : 30316	Material : N/A
Written By : <u>JS 07.01.18</u>	Due Date : 1/30/2007 Qty: 1 Um: Each
Checked & Approved By : <u>JS 07.01.18</u>	
Comment : Est Rev: F 05.09.01 Add holes for compatibility with Bell Skidtubes KJ/JLM	

Additional Product

Job Number:



Seq. #:	Machine Or Operation:	Description :
----------------	------------------------------	----------------------

1.0	DC	DOCUMENT CONTROL
-----	----	------------------

**Comment:** DOCUMENT CONTROL

Photocopy bluefile and create labels as per PPP D206-667-201 CHG002 ✓

JS 07.01.18 (1)

2.0	D6003102	Crosstube
-----	----------	-----------

**Comment:** Qty.: 1.0000 Each(s)/Unit Total : 1.0000 Each(s)

Pick:

Qty Part number Description Batch

1 D6003-102 Crosstube 23967

Check OD = 2.250"; ID = 1.380"

MS 07/01/21

3.0	MORI SEIKI	MORI SEIKI CNC LATHE LARGE
-----	------------	----------------------------

**Comment:** MORI SEIKI CNC LATHE LARGE

1-Fill tube with sand & install plugs DT8534 on both ends as per Folio FA084

2-Turn first side as per Folio FA084

3-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D206-667-241.

MS 07/01/21

4.0	QC1	INSPECT ALL DIM TO DIM SHEET
-----	-----	------------------------------

**Comment:** INSPECT ALL DIM TO DIM SHEET

MS 07/01/21

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Thursday, 1/18/2007 3:21:00 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 206B AFT X-TUBE

Job Number: 30318

Part Number: D206667201

Job Number:



Seq. #:

Machine Or Operation:

Description :

5.0

MORI SEIKI

MORI SEIKI CNC LATHE LARGE



Comment: MORI SEIKI CNC LATHE LARGE

1-Turn second side as per Folio FA084

2-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D206-667-241.

3-Remove sand and plugs

4-Scribe part # and batch # using vibrating stylus as per Dwg D206-667-241

Inside of Cuff(Donot engrave on outside of tube)

MS 07/01/22 1

6.0

QC1

INSPECT ALL DIM TO DIM SHEET



Comment: INSPECT ALL DIM TO DIM SHEET

MS 07/01/22 1

7.0

QC8

SECOND CHECK



Comment: SECOND CHECK

BC 07.01.23 1

8.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Polish entire outside surface of crosstube

S/M 07-01-30

9.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

DP 7-1-30

10.0

HAND FINISHING1

HAND FINISHING RESOURCE #1



Comment: HAND FINISHING RESOURCE #1

Chemical Conversion Coat as per QSI 005 4.1

S/M 07-01-30

11.0

BENDING

BENDING MACHINE



Comment: BENDING MACHINE

Bend tube as per Dwg D206-667-241 using CNC bender program 206B-AF and Folio FT

EL 7-5-8

W/O:		WORK ORDER CHANGES						
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector	

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____
 QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: 8/2007 3:21:00 PM
User: .n

Process Sheet

Custo: J-DAR001 Dart Helicopters Services

Drawing Name: 206B AFT X-TUBE

Job Number: 30318

Part Number: D206667201

Job Number:



Seq. #:

Machine Or Operation:

Description :

12.0

QC6

DIMENSIONAL CHECK



Comment: DIMENSIONAL CHECK

Handwritten: 07-05-16 @

13.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Drill pilot holes (3/16") as per Dwg D206-667-241 using drill Jig DT8575 & DT8576

2-Drill & ream holes as per Dwg D206-667-241 using drill Jig DT8575 & DT8576.

(DRILL 3 HOLES ON BOTH SIDES)

3-Flip tube and switch drilling Jigs from right to left, left to right. Locate tube using "T" pins off holes drilled in previous step.

4-Drill pilot holes (3/16") as per Dwg D206-667-241 using drill Jig DT8575 & DT8576

5-Drill & ream holes as per Dwg D206-667-241 using drill Jig DT8575 & DT8576. Check dimensions between holes on all four sides to ensure proper alignment. Use DT8583 & 8584 SUPPORT Jigs.
(DRILL 3 HOLES ON BOTH SIDES)

6-Drill rivet holes as per Dwg D206-667-241 using drill Jig DT8788

7-Grind sink holes as per Dwg D206-667-241

8-Deburr & Inspect for surface damage. Repair damage within limits as per Dwg D206-667-241

Handwritten: JB 7-6-18

14.0

HAND FINISHING1

HAND FINISHING RESOURCE #1



Comment: HAND FINISHING RESOURCE #1

Chemical Conversion Coat as per QSI 005 4.1

Handwritten: JB 7-6-18

15.0

QC3

INSPECT POWDER COAT/CHEMICAL CONVERSION



Comment: INSPECT POWDER COAT/CHEMICAL CONVERSION

Handwritten: 07-06-20 @

16.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

Handwritten: 07-06-20 @

Dart Aerospace Ltd
W/O:

WORK ORDER CHANGES

DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____
 QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Thursday, 1/18/2007 3:21:00 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 206B AFT X-TUBE

Job Number: 30318

Part Number: D206667201

Job Number:



Seq. #:

Machine Or Operation:

Description :

17.0

OUTSIDE SERVICE

OUTSIDE SERVICES



Comment: Sub-Contracting OUTSIDE SERVICES

Liquid Penetrant Inspection as per QSI 038Or

Issue P/O: 4012

LPI as per ASTM 1417

Level 2 Attach copy of NDT results to work order

C2067/06/21 ①

18.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Inspect for transit damage

Ensure copy of NDT results attached to work order.

07/06/26 ①

19.0

QC6

DIMENSIONAL CHECK



Comment: Inspect for damage & ensure results are as per Dwg D206-667-103

07/06/27 ①

20.0

SPRAY PAINTING

SPRAY PAINTING



Comment: SPRAY PAINTING

1-Mask Threaded holes

2-Prime inside and outside crosstube as per QSI 005 4.2

3-Paint outside crosstube with White Imron as per QSI 005 4.2

07-07-19

21.0

QC14

Inspect Spray Paint



Comment: Inspect Spray Paint

Wrap in plastic bag to protect from scratches

ml 0707 22

①

22.0

D2856400

Abrasion Strip



Comment: Qty.: 1.3525 f(s)/Unit Total : 1.3525 f(s)

Pick:

Qty Part number Description Batch

2 D2856-400(Cut to 7.73") Abrasion Strip

32020 ml 0707 22

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Thursday, 1/18/2007 3:21:00 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 206B AFT X-TUBE

Job Number: 30318

Part Number: D206667201

Job Number:



Seq. #:

Machine Or Operation:

Description :

23.0

D28911

Support 2.25 dia



Comment: Qty.: 2.0000 Each(s)/Unit Total: 2.0000 Each(s)

Pick:

Qty Part number Description Batch

2 D2891-1

Support

28388

ml 07 07 22

24.0

MS2192020

Clamp (per MIL-DTL-8783C)



Comment: Qty.: 4.0000 Each(s)/Unit Total: 4.0000 Each(s)

Pick:

Qty Part number Description Batch

4 MS21920-22

Clamp

104902

ml 07 07 22

25.0

LANDING GEAR 1

LANDING GEAR RESOURCE 1



Comment: LANDING GEAR RESOURCE 1

1-Install abrasion strips as per QSI 035 using DT8579.

2-Install supports and clamps as per Dwg D206-667-241. Torque clamps to 80-100 in lb

ml 07 07 22

26.0

QC5

INSPECT WORK TO CURRENT STEP



Comment: INSPECT WORK TO CURRENT STEP

ml 07 07 24 (41)

27.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Pick Packing Kit

28.0

AN532A

Bolt



Comment: Qty.: 4.0000 Each(s)/Unit Total: 4.0000 Each(s)

Bolt

M103481

EP

29.0

D2872043

Nut Plate Assembly



Comment: Qty.: 2.0000 Each(s)/Unit Total: 2.0000 Each(s)

Pick:

Qty Part number Description Batch

2 D2872-043

Nut Plate

B24151

EP

EP 07 07 24

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Thursday, 1/18/2007 3:21:01 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 206B AFT X-TUBE

Job Number: 30318

Part Number: D206667201

Job Number:



Seq. #:

Machine Or Operation:

Description :

30.0

D2872045

Nut Plate Assembly



Comment: Qty.: 2.0000 Each(s)/Unit Total : 2.0000 Each(s)

Pick:

Qty Part number Description Batch

2 D2872-045 Nut Plate P24152 ✓

31.0

AN510A

Bolt



Comment: Qty.: 10.0000 Each(s)/Unit Total : 10.0000 Each(s)

Pick:Packing Kit

Qty Part number Description Batch

10 AN5-10A Bolt M102959 ✓

32.0

AN530A

BOLT



Comment: Qty.: 10.0000 Each(s)/Unit Total : 10.0000 Each(s)

Pick:Packing Kit

Qty Part number Description Batch

10 AN5-30A Bolt M103389 ✓

33.0

AN960JD516

Washer



Comment: Qty.: 20.0000 Each(s)/Unit Total : 20.0000 Each(s)

Pick:Packing Kit

Qty Part number Description Batch

20 AN960JD516 Washer M104156 ✓

34.0

MS21042L5

Nut



Comment: Qty.: 10.0000 Each(s)/Unit Total : 10.0000 Each(s)

Pick:Packing Kit

Qty Part number Description Batch

10 MS21042L5 NUT M103830 ✓

35.0

QC4

INSPECT 100% KITS FOR COMPLETENESS



Comment: INSPECT 100% KITS FOR COMPLETENESS

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes ☒ No ☐ DQA: 12 Date: 07/07/24
 QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Date: Thursday, 1/18/2007 3:21:01 PM
User: Kim Johnston

Process Sheet

Customer: CU-DAR001 Dart Helicopters Services

Drawing Name: 206B AFT X-TUBE

Job Number: 30318

Part Number: D206667201

Job Number:



Seq. #:

Machine Or Operation:

Description :

36.0

PACKAGING 1

PACKAGING RESOURCE #1



Comment: PACKAGING RESOURCE #1

Identify and pack for shipping as per PPP D206-667-201

Location: _____

PPP Rev: D

Ep 507/07/240 CD

37.0

QC21

FINAL INSPECTION/W/O RELEASE



Comment: FINAL INSPECTION/W/O RELEASE

57/07/24

Job Completion



W 07.07.24

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DART AEROSPACE LTD	Work Order:	30318
Description: Crosstube Assembly	Part Number:	D206-667-241
Inspection Dwg: D206-667-241 Rev: B		Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST


☒ First Article ☐ Prototype

Inspection Sheet Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
SIDE A	30° x 0.500	+/-0.010	30° x .500	✓		
	0.250	+/-0.010	.250	✓		
	2.240	+0.005/-0.000	2.244	✓		
	4.438	+/-0.030	4.440	✓		
	1.780	+0.005/-0.000	1.783	✓		
	R0.063	+/-0.010	.063	✓		
	1.851	+0.005/-0.000	1.854	✓		
	1.928	+0.005/-0.000	1.931	✓		
	2.005	+0.005/-0.000	2.009	✓		
	2.082	+0.005/-0.000	2.086	✓		
	2.159	+0.005/-0.000	2.163	✓		
	2.190	+0.005/-0.000	2.194	✓		
SIDE B	30° x 0.500	+/-0.010	30° x .500	✓		
	0.250	+/-0.010	.250	✓		
	2.240	+0.005/-0.000	2.243	✓		
	4.438	+/-0.030	4.440	✓		
	1.780	+0.005/-0.000	1.783	✓		
	R0.063	+/-0.010	.063	✓		
	1.851	+0.005/-0.000	1.853	✓		
	1.928	+0.005/-0.000	1.932	✓		
	2.005	+0.005/-0.000	2.009	✓		
	2.082	+0.005/-0.000	2.086	✓		
	2.159	+0.005/-0.000	2.163	✓		
	2.190	+0.005/-0.000	2.194	✓		
	100.60	+/-0.020	100.60	✓		

Measured by:	MS	Audited by:	SG	Prototype Approval:	N/A
Date:	07/01/21	Date:	07.01.23	Date:	N/A

Rev	Date	Change	Revised by	Approved
A	06.10.16	New Issue (P/O D206-667-201)	KJ/JLM	BE

Crosstube Bend Dimension Sheet

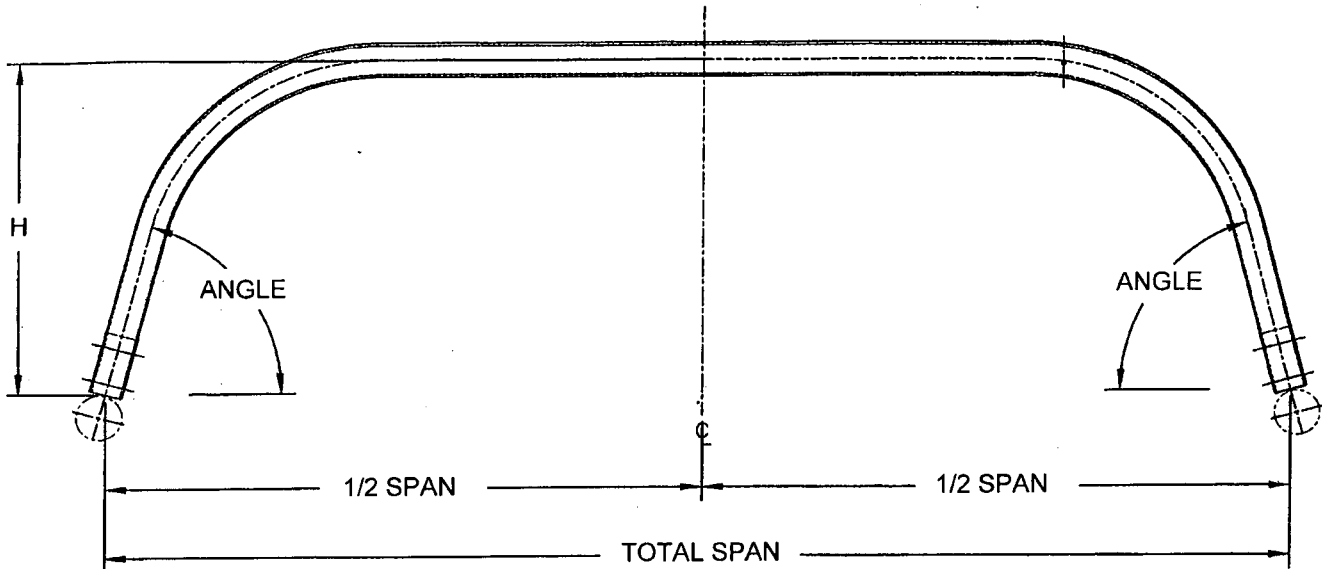

PART NUMBER: _____

BATCH NUMBER: 30318

DRAWING: _____ REVISION: _____

H: _____

1/2 SPAN: _____


TOTAL SPAN: _____

ANGLE: _____

QC 15: _____

DATE: _____

QTY: _____

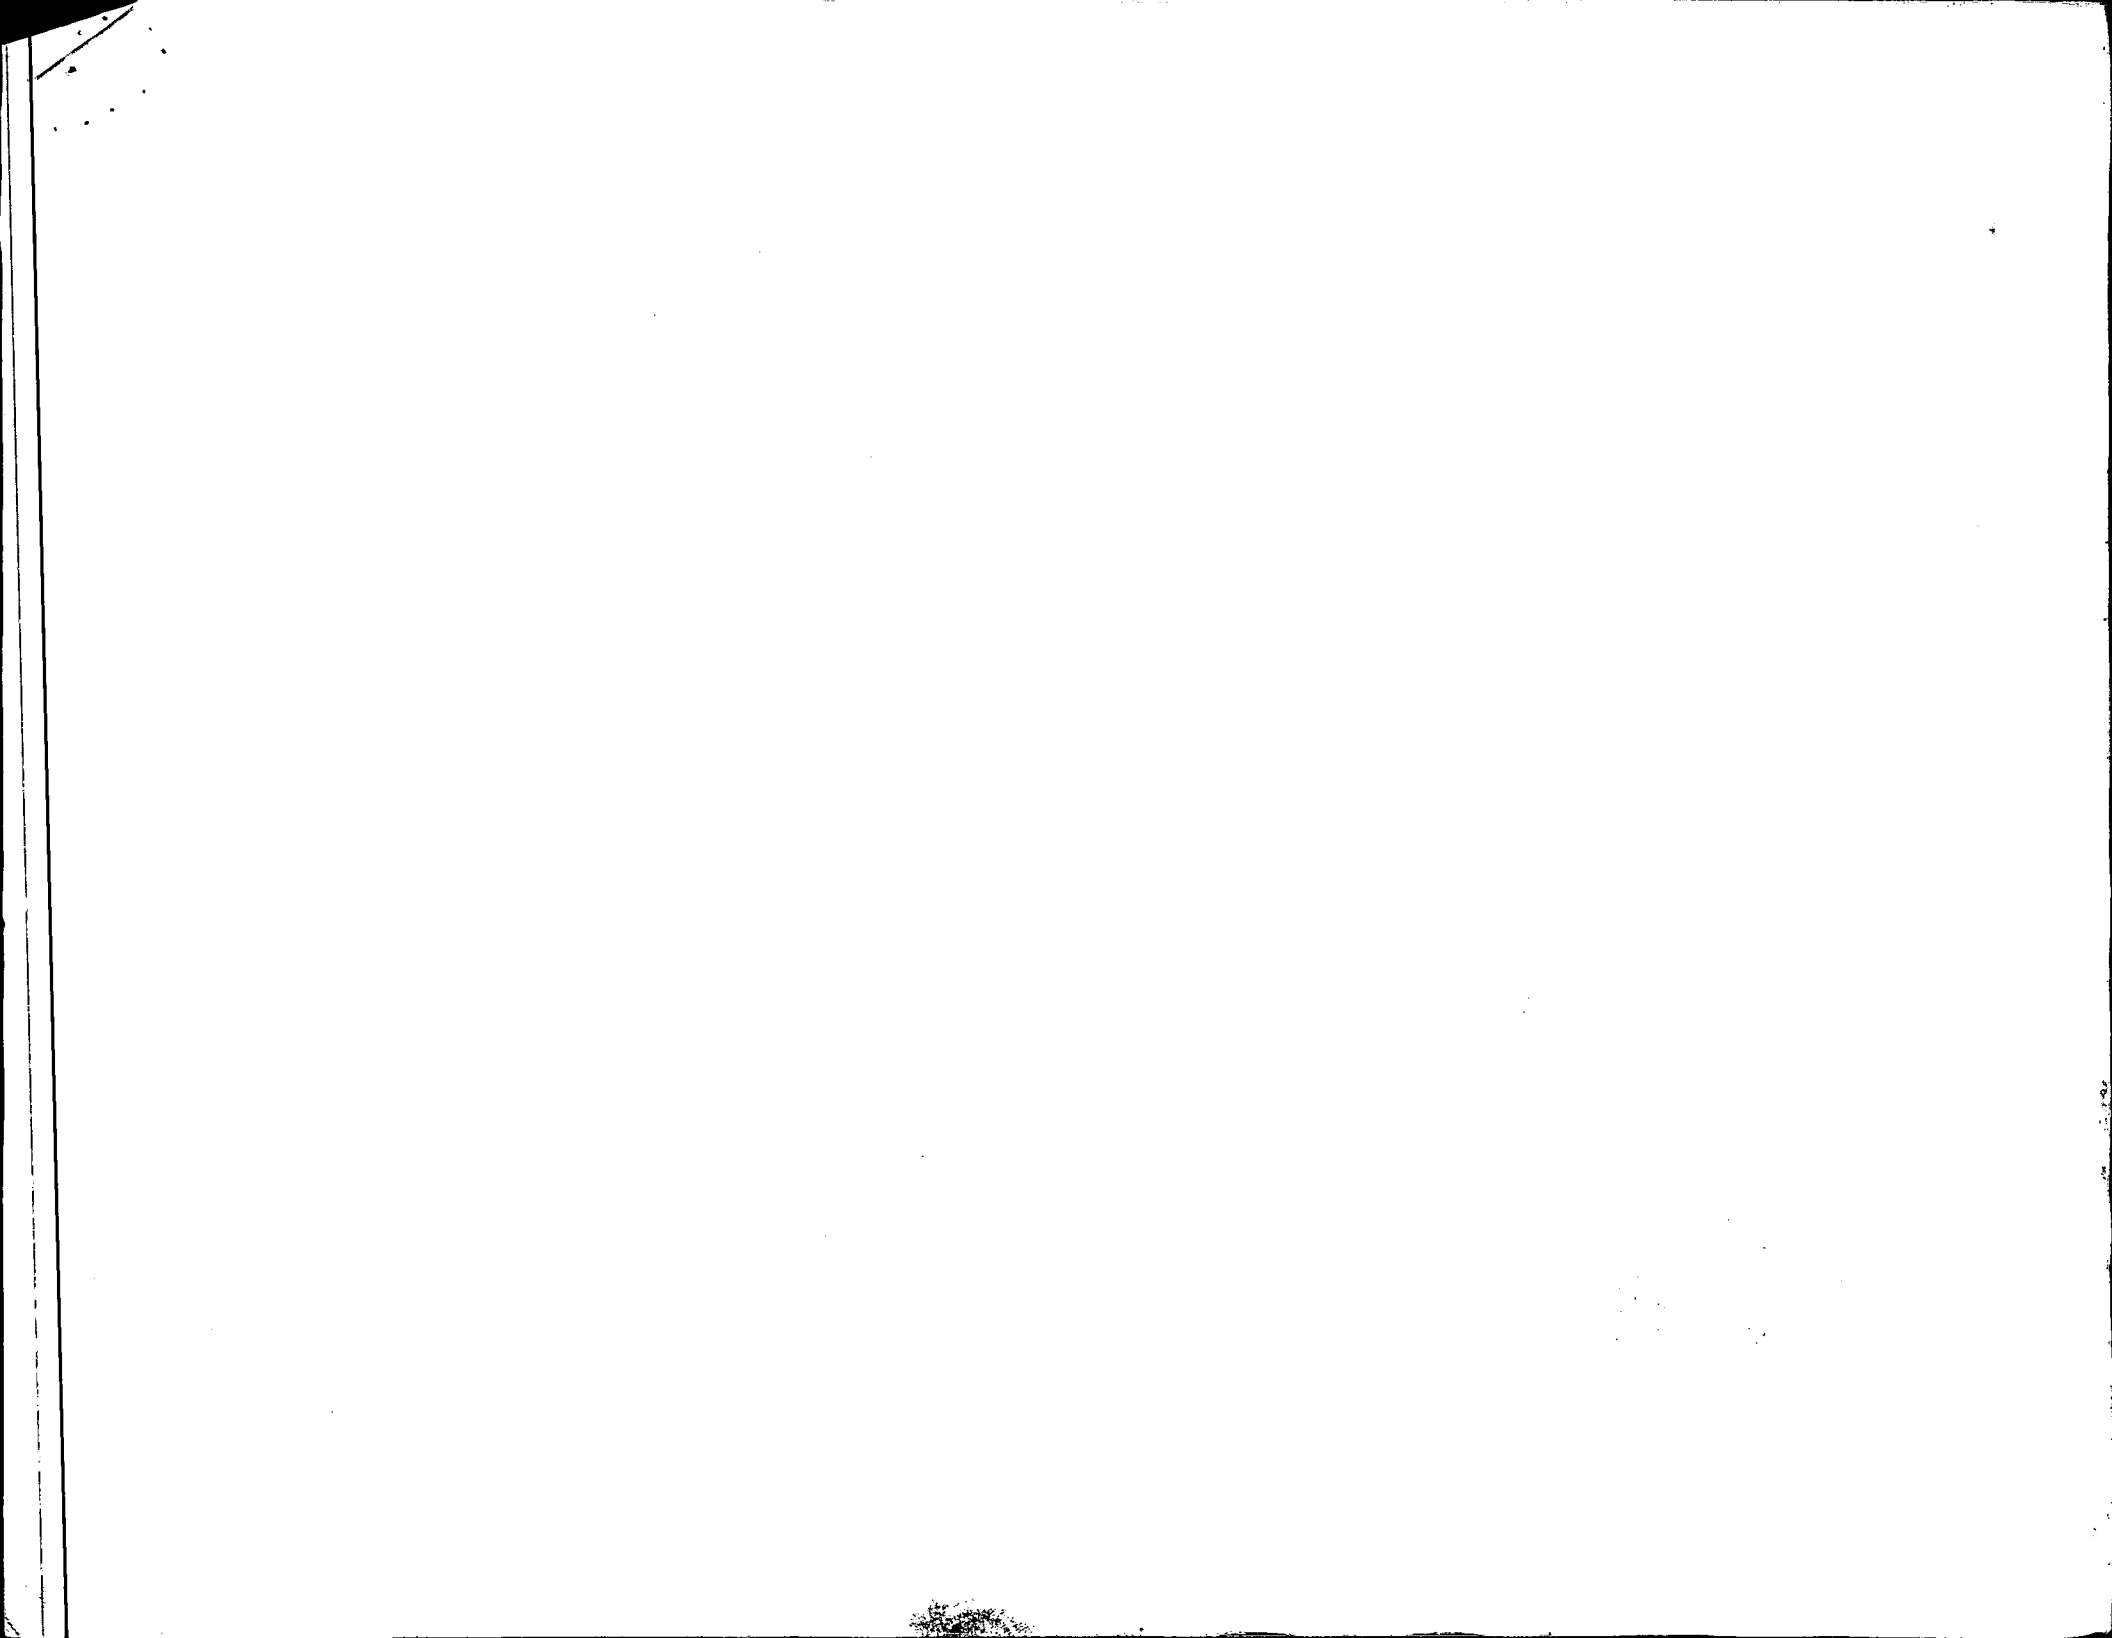

DART

DESIGN PH	DRAWN BY PH	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED [Signature]	APPROVED [Signature]	DRAWING NO. D206-667-241	REV: B SHEET 1 OF 3
DATE 05.02.04		TITLE CROSSTUBE ASS'Y (206B HIGH AFT) NTS	
A	00.11.17	NEW ISSUE	
B	05.02.04	ADD HOLES FOR COMPATABILITY WITH BHT/AA SKIDTUBES	

RELEASED
05-06-16 [Signature]

Qty	Part Number	Description
X	D206-667-241	CROSSTUBE ASSEMBLY (206B HIGH AFT)
1	D6003-102	CROSSTUBE
2	D2856-400-694	ABRASION STRIP
2	D2891-1	SUPPORT
4	MS21920-20	CLAMP


GENERAL NOTES:


- 1) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 2) MATERIAL: MANUFACTURED FROM D6003-102
FINISHED LENGTH = 100.60±0.020
- 3) FINISH: CHEMICAL CONVERSION COAT PER DART QSI 005 4.1
PRIME INSIDE AND OUTSIDE PER DART QSI 005 4.2
PAINT OUTSIDE PER DART QSI 005 4.2
- 4) PART IS SYMMETRIC ABOUT CENTERLINE
- 5) RUN-OFF PART. BLEND OUT EDGE LONGITUDINALLY, TRANSITION SHOULD BE SMOOTH.
- 6) BEND PROGRESSIVELY WITH A MINIMUM OF 12 PASSES. MAXIMUM TUBE FLATTENING DUE TO BENDING IS 6% BASED ON O.D.
- 7) LIQUID PENETRANT INSPECT OUTSIDE SURFACE OF CROSSTUBE PER QSI 038.
- 8) SCRIBE DART PART NUMBER AND BATCH NUMBER IN THIS AREA WITH VIBRATING STYLUS.
- 9) INSTALL D2856-400-694 ABRASION STRIP WITH A 0.13 (REF) GAP ON BOTTOM SIDE OF CROSSTUBE, CENTERED OPPOSITE D2891-1 SUPPORT, PER QSI 035.
- 10) EXTREME CARE MUST BE TAKEN TO PROTECT THE OUTSIDE SURFACE OF THE TUBE. THE OUTSIDE SURFACE MUST BE SMOOTH AND FREE FROM SURFACE DEFECTS SUCH AS SCRATCHES, NICKS, OR DENTS. DEFECTS UP TO 0.005" MAY BE BLENDED OUT LONGITUDINALLY. CIRCUMFERENTIAL GRIND MARKS ARE UNACCEPTABLE.
- 11) IT IS OPTIONAL TO SEAL EDGES OF SUPPORTS AND ABRASION STRIP USING SIKAFLEX 241/291 SEALANT.
- 12) TORQUE CLAMPS 80 TO 100 IN-LB.

UNCONTROLLED COPY
ENGINEERING
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 30318

Copyright © 2000 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

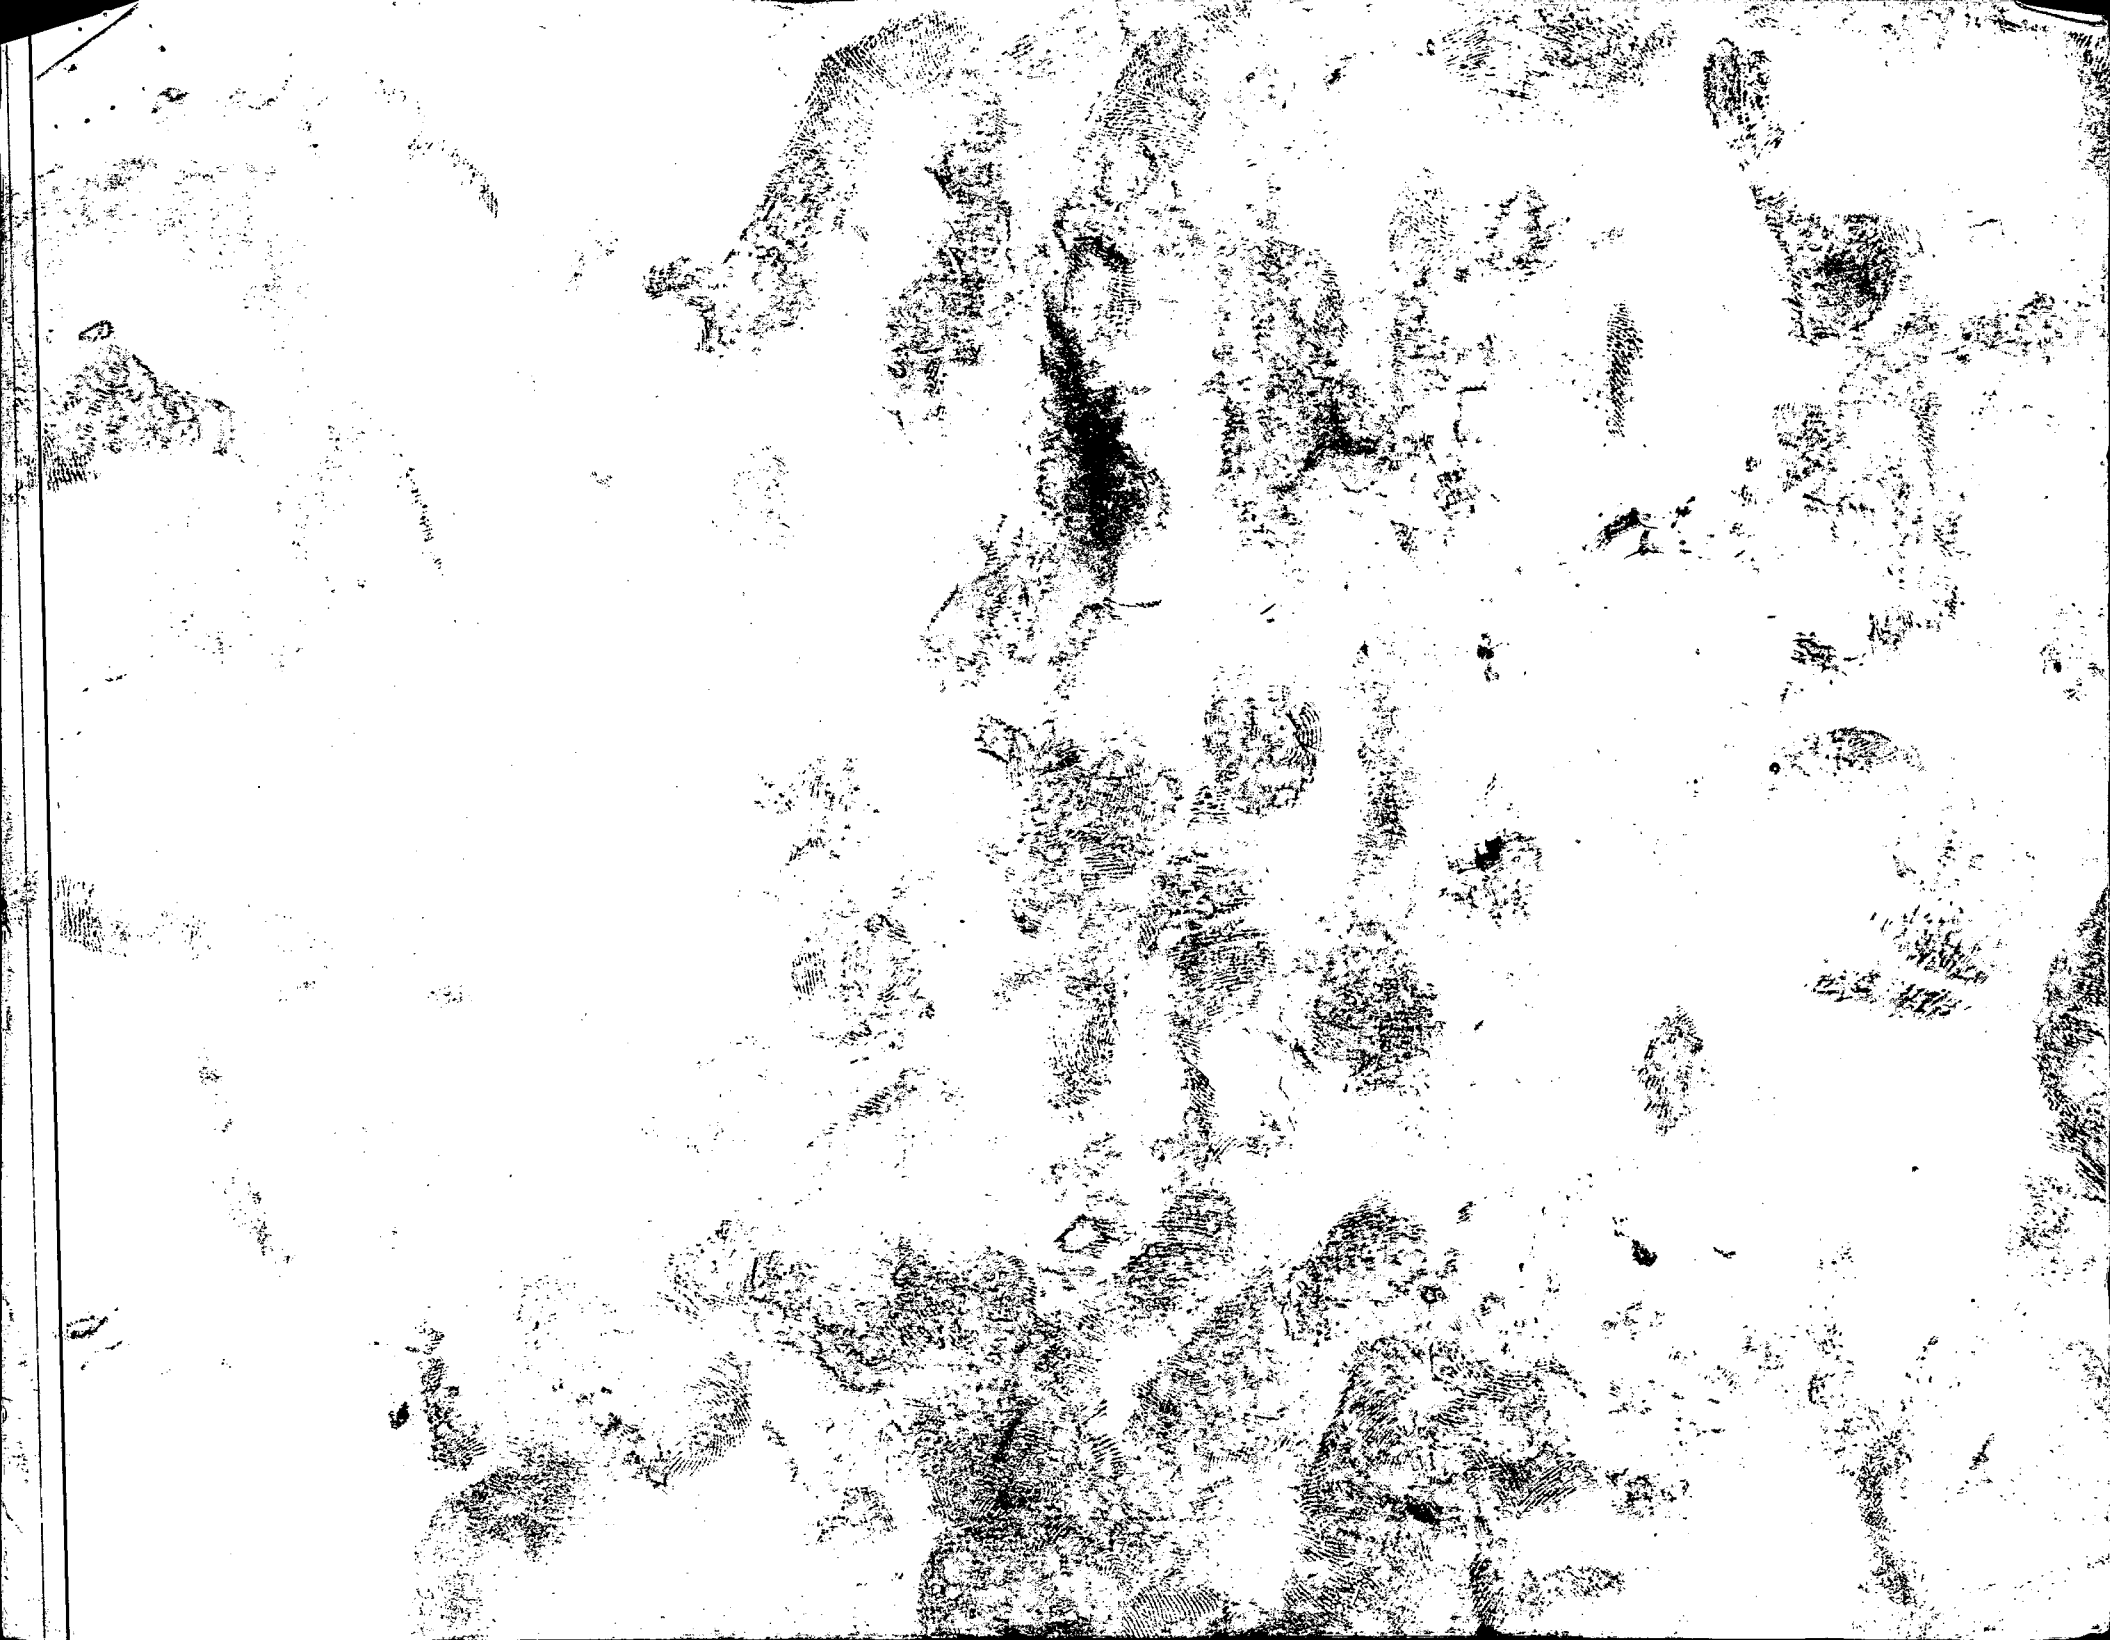


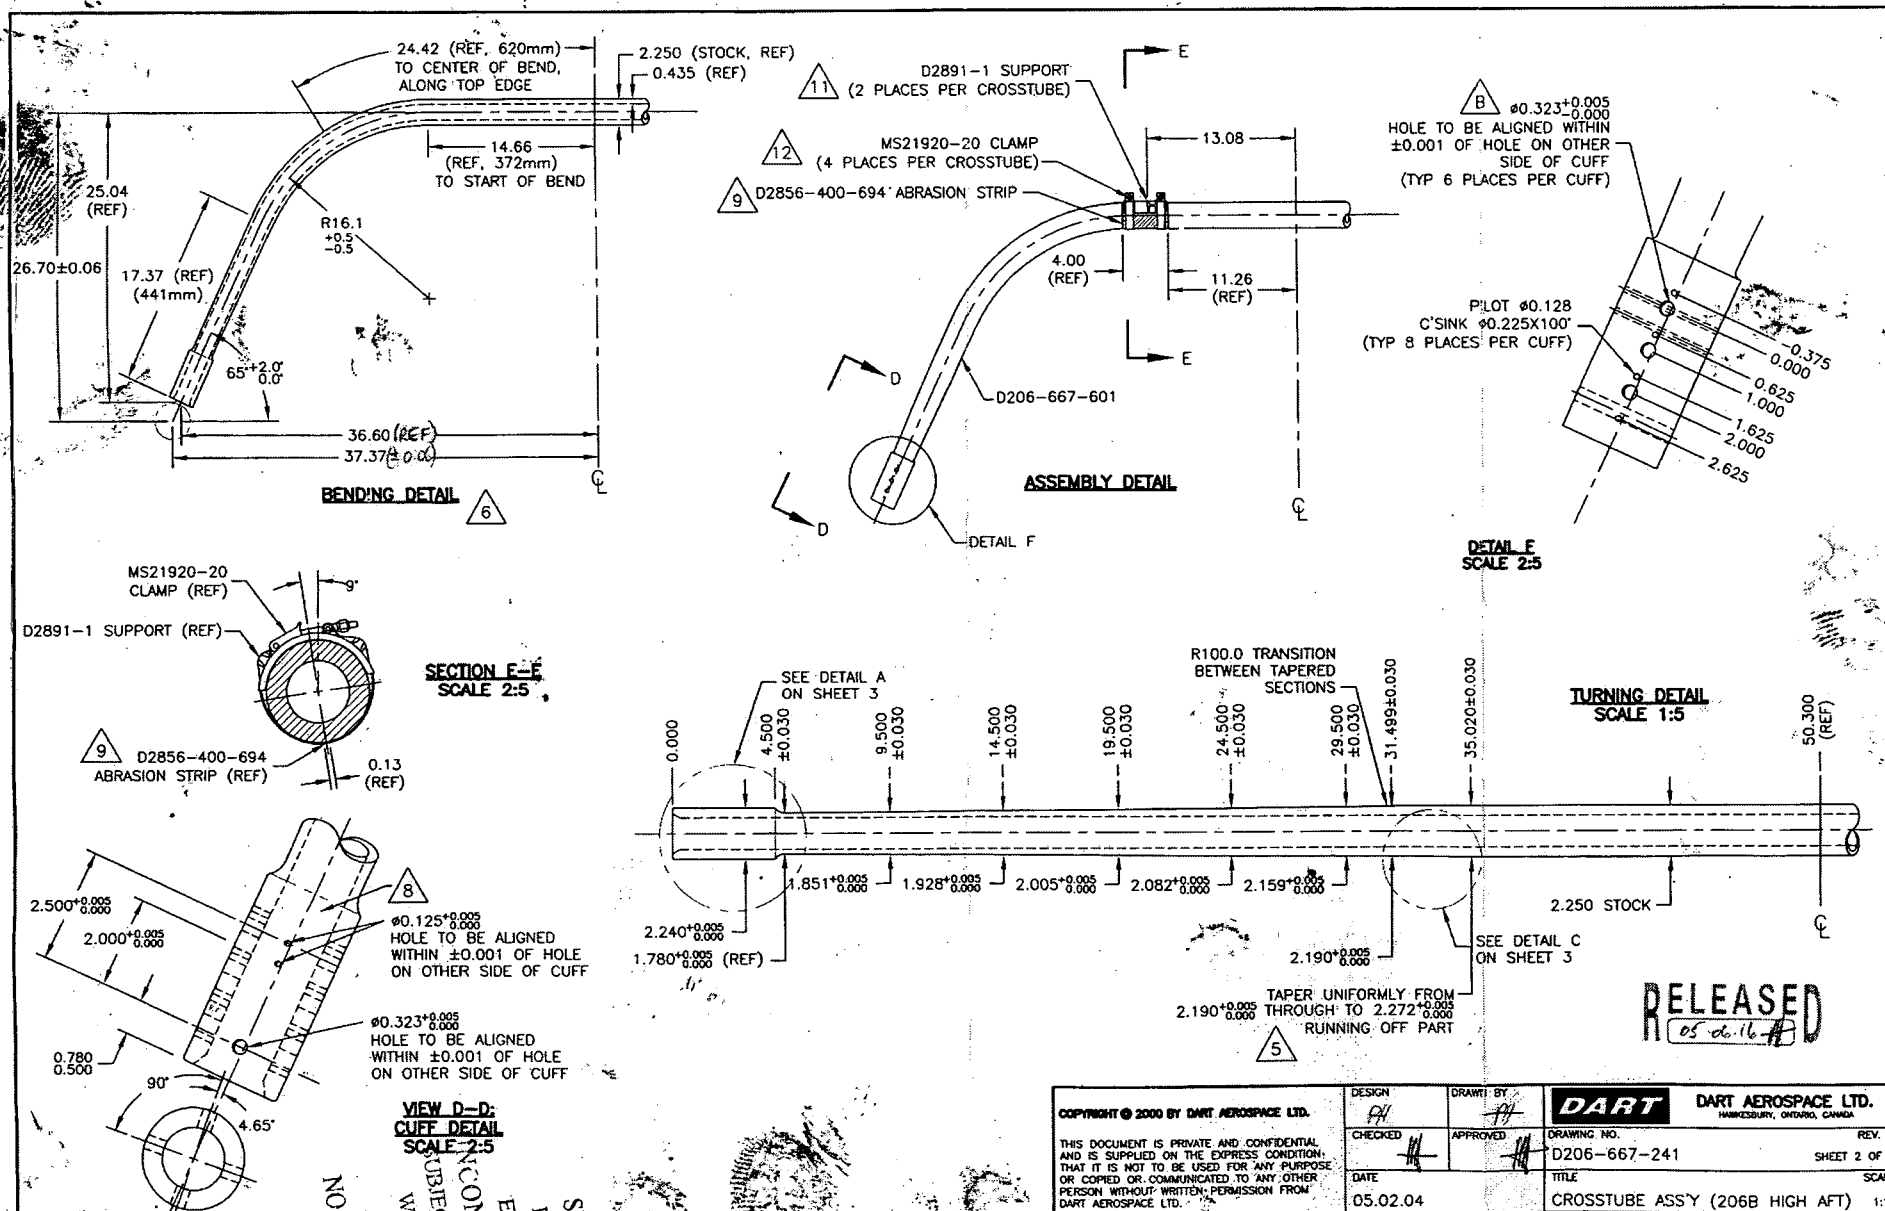


COPYRIGHT © 2000 BY DART AEROSPACE LTD.		DESIGN	DRAWN BY	DART DART AEROSPACE LTD. HAMMERSBURY, ONTARIO, CANADA	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		CHECKED	APPROVED	DRAWING NO. D206-667-241	REV. B SHEET 2 OF 3
DATE 05.02.04		TITLE CROSSTUBE ASS'Y (206B HIGH AFT)		SCALE 1:10	

NO. 30318
 WORK ORDER
 SUBJECT TO AMENDMENT
 WITHOUT NOTICE
 CONTROLLED COPY
 ENGINEERING
 RETURN TO
 SHOP COPY


RELEASED
05-06-16

DETAIL A: CROSSTUBE CUFF

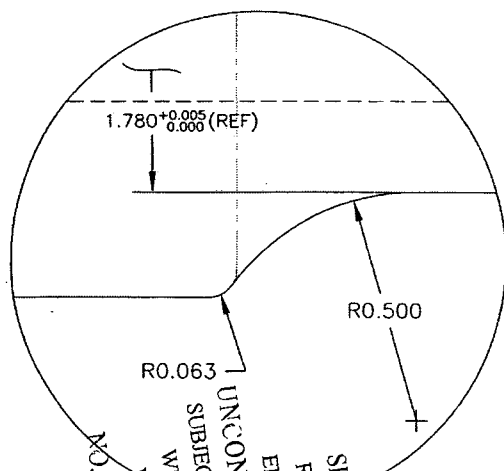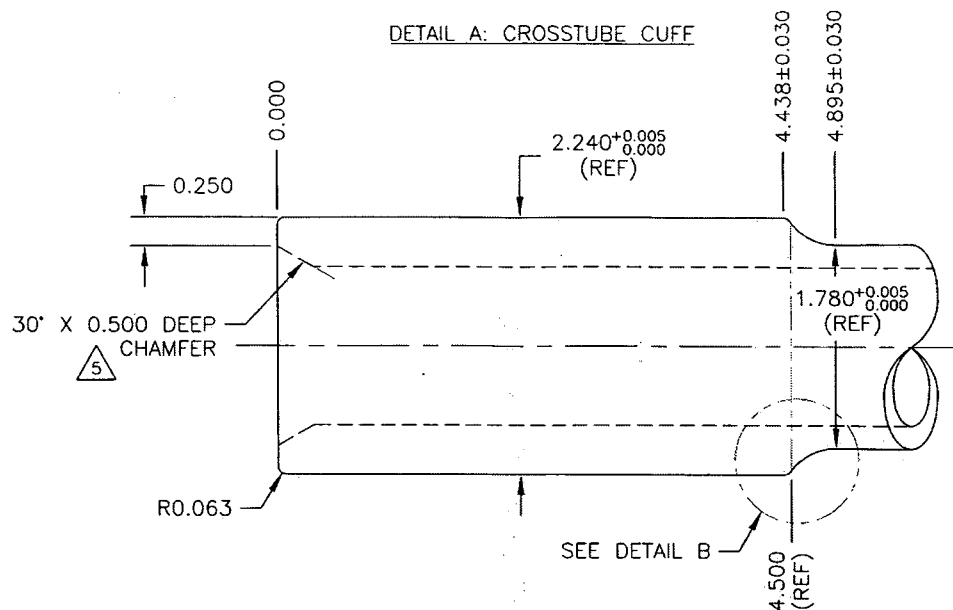

DETAIL B: CUFF
TRANSITION
SCALE 4:1

DETAIL C:
TAPER RUN-OFF
NOT TO SCALE

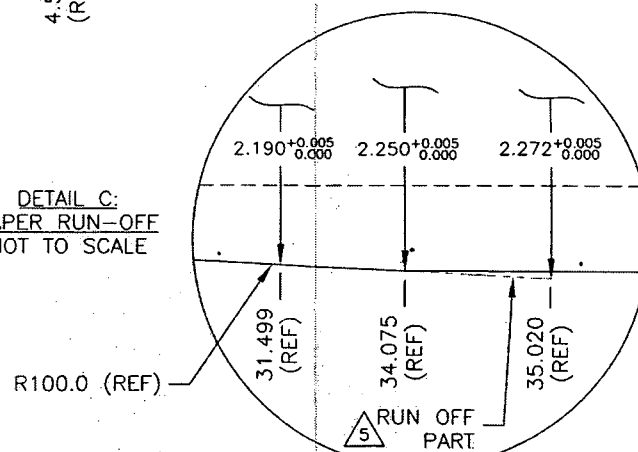


NO. 30318
WORK ORDER
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
RETURN TO
ENGINEERING
SHOP COPY

COPYRIGHT © 2000 BY DART AEROSPACE LTD.		DESIGN	PH	DRAWN BY	PH	DART	DART AEROSPACE LTD.
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.		CHECKED	PH	APPROVED	PH	DRAWING NO.	REV. B
		DATE	05.02.04			D206-667-241	SHEET 3 OF 3
		TITLE				CROSSTUBE ASS'Y (206B HIGH AFT)	SCALE 1:1



DART AEROSPACE LTD		Work Order:	30318
Description: Crosstube High Aft (206B)		Part Number:	D206-667-201
Inspection Dwg: D206-667-241 Rev: B		Page 1 of 1	

Required Dimension	Min	Max
Height	24.48	25.10
1/2 Span	36.54	36.66
Angle	65	67
Total Span	73.08	73.32

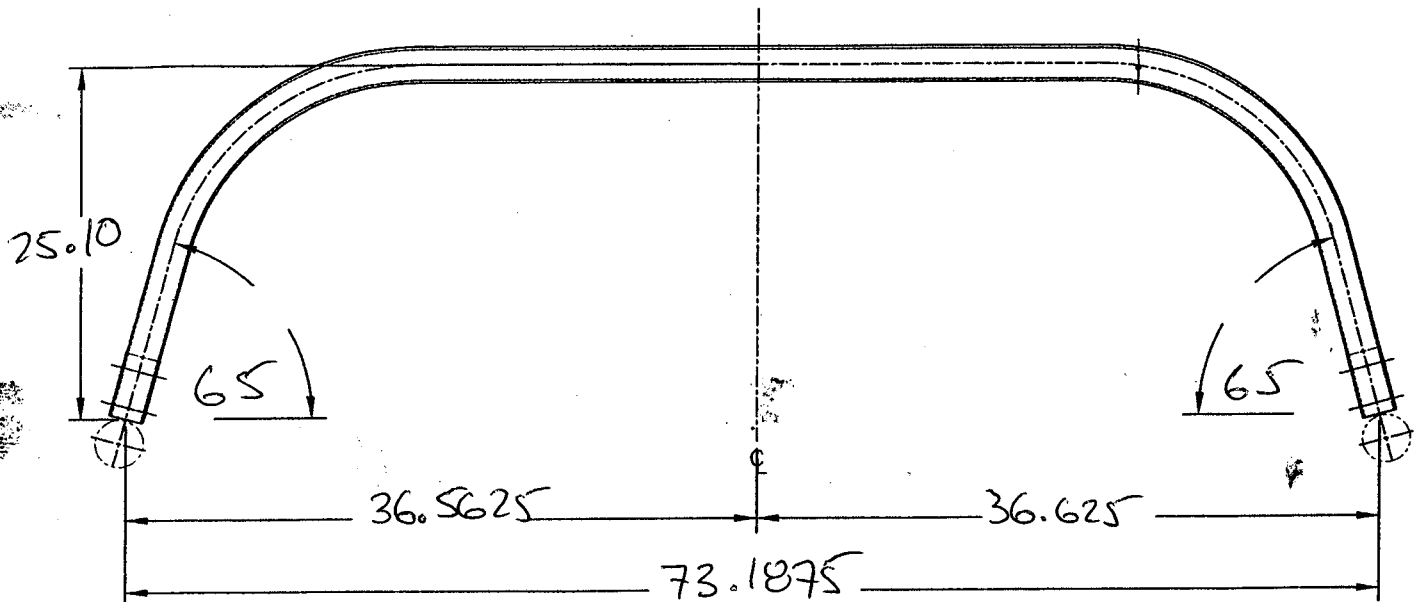


Comments

QC15 Inspection	<i>[Signature]</i> 07.05.06
Date	

Rev	Date	Change	Revised by	Approved
A	07.02.06	New Issue	KJ/JM	<i>[Signature]</i>





HeathAir

INTERNATIONAL (1991) INC.

681 Ave. Lepine, Dorval, Québec H9P 1G3
Tél.: (514) 636-1000 • Fax: (514) 636-0031

W.O. N° 36755

A.M.O. Number: 46/90

NON-DESTRUCTIVE TESTING REPORT

AIRCRAFT / COMPONENT INFORMATION

REGISTRATION:

MODEL/TYPE:

SERIAL NUMBER:

TOTAL HR/LDG:

OPERATED BY:

BASED AT:

INSPECTION REQUIREMENTS

Carry out FPI of (16) cross tube (external surface) as per ASTM E-1417-05 and the Dart QSI 038, Section 4.1.1 (on file at client) - parts delivered to HeathAir.

Qty (3) P/N D206-667-201 S/N's B30318, B30442 & B30441

Qty (4) P/N D206-667-203BL S/N's B32672, B32458, B32671 & B32457

Qty (1) P/N D407-667-205 S/N B31040

Qty (1) P/N D206-667-201 S/N B30440

Qty (4) P/N D212-664-201 S/N's B32148, B32146, B32149 & B32147

Qty (3) P/N D206-667-103BL S/N's B32667, B32455 & B32456

☐ RADIOGRAPHY

☐ ULTRASONIC

☒ PENETRANT

☐ MAGNETIC PARTICLE

☐ EDDY CURRENT

INSPECTION REPORT

Fluorescent penetrant inspection was performed in accordance with the above requirements on (16) cross tubes.

Note: A Level 3 penetrant was substituted for the requested Level 2 (3 is more sensitive)
Ardrox 970P25E Batch #04B503.

All (16) cross tubes passed inspection.

THE MAINTENANCE DESCRIBED ABOVE HAS BEEN PERFORMED IN ACCORDANCE WITH
THE APPLICABLE STANDARDS OF AIRWORTHINESS

INSPECTED BY:

S. FLECHER

DATE

June 22, 2007

INSPECTION
STAMP(S)

Not Required

CUSTOMER INFORMATION

CUSTOMER: Dart Aerospace

P.O. NUMBER

4012

ADDRESS:

CONTACT NAME:

Chantel

LABOUR

@

\$

MATERIALS

@

TRAVEL EXPENSES

@

GST

HOTEL EXPENSES

@

PST

INVOICE NO.

TOTAL \$

WHITE COPY - INSPECTION FILE • YELLOW COPY - CUSTOMER • PINK COPY - ACCOUNTANT
